



**TOGETHER**  
*for a sustainable future*

## OCCASION

This publication has been made available to the public on the occasion of the 50<sup>th</sup> anniversary of the United Nations Industrial Development Organisation.



**TOGETHER**  
*for a sustainable future*

## DISCLAIMER

This document has been produced without formal United Nations editing. The designations employed and the presentation of the material in this document do not imply the expression of any opinion whatsoever on the part of the Secretariat of the United Nations Industrial Development Organization (UNIDO) concerning the legal status of any country, territory, city or area or of its authorities, or concerning the delimitation of its frontiers or boundaries, or its economic system or degree of development. Designations such as “developed”, “industrialized” and “developing” are intended for statistical convenience and do not necessarily express a judgment about the stage reached by a particular country or area in the development process. Mention of firm names or commercial products does not constitute an endorsement by UNIDO.

## FAIR USE POLICY

Any part of this publication may be quoted and referenced for educational and research purposes without additional permission from UNIDO. However, those who make use of quoting and referencing this publication are requested to follow the Fair Use Policy of giving due credit to UNIDO.

## CONTACT

Please contact [publications@unido.org](mailto:publications@unido.org) for further information concerning UNIDO publications.

For more information about UNIDO, please visit us at [www.unido.org](http://www.unido.org)



---

**CONTRACT NO. 16002215**

**FINAL REPORT**

**REHABILITATION  
OF  
AL-HADBAA ASSOCIATION FOR THE DISABLED**

**LOCATED IN MOSUL DISTRICT  
NINEWA GOVERNORATE-IRAQ**





UNITED INDUSTRIAL DEVELOPMENT ORGANIZATION  
ORGANISATION DES NATIONS UNIES POUR LE DEVELOPPEMENT INDUSTRIEL

ACCEPTANCE CERTIFICATE

**Project No.:** TE/IRQ/09A08  
**Contractor Name:** EDEN ENGINEERING COMPANY  
**Start Date:** 17, AUGEST 2010  
**End Date:** 15, OCTOBER 2010  
**Site Location:** Mosul District - NINEWA GOVERNORATE

**WHEREAS**

The United Nations Industrial Development Organization hereinafter referred to as the "Organization", and the firm **EDEN AL ENGINEERING COMPANY**, hereinafter referred to as the "Contractor", which has been awarded by UNIDO a contract "Rehabilitation of Al-HADBAA Association for Disabled" hereinafter referred to as the "Contract". The Contractor has completed all of the Works as set out in detail in the Contract in accordance with the specifications and at the sites set out therein.

**NOW THEREFORE**

We the undersigned, in our capacity as members of the Organization's Technical Committee, having supervised the completion of the Works and having duly undertaken all necessary inspections and verifications of such Works in accordance with the rule and regulations of our profession, confirm that the Works mentioned below have been completed in full compliance with the relevant specifications, plans and drawings of the Contract and the laws and regulations of the country where such Works have been undertaken, on the date of signature of this certificate, except for the reservations set out below, if any.

**Members of the Technical Committee of the Organization, End User and Contractor Rep:**

**United Nation Industrial Development Organization (or his Designate):**

Eng. Saifuldeen R. Ibrahim Al Shbeeb

Signature: \_\_\_\_\_

Date: 17 October 2010

**Al Hadbaa Association Director Assistant (or his Designate):**

Mr. Hany Abdulghafor Ahmed

Signature: \_\_\_\_\_

Date: 17 October 2010

**Al Hadbaa Association Civil Engineer**

Eng. Anas Younis Mahmoud

Signature: \_\_\_\_\_

Date:

**Production Group (Al Hadbaa Association Director)**

Manager: Nadima Ibrahim Mactom

Signature: \_\_\_\_\_

Date: 17 October 2010


**Contractor Representative:**


EDEN ENGINEERING COMPANY

Mr. Mohialdeen K. Kawther

Signature: \_\_\_\_\_

Date: 17 October 2010





**Eden Engineering Co.**  
**Mosul – Alzeraee Av.**  
**07701614472 – 07481701368**  
**Edeneng2004@yahoo.com**


Invoice No: 4

UNIDO  
Programme Support and General Management Division  
Operational Support Services  
Procurement Services Unit  
P.O. Box 300  
A-1400 Vienna  
Austria

Date: 20/10/2010

UNIDO Project No:	TE/IRQ/09/A08	UNIDO Contract No.	16002215
Payment Upon:	Receipt and acceptance of the contractors final report	The amount of US\$	18,308


Bank name:	Mosul bank for development & Investment
Bank name:	Main branch
Bank Account:	289089.282.840.00.0001/ Eden Engineering Company
Swift Code:	MOUIQBA
Intermediary Bank Name:	The housing bank for trade& finance-Amman-Jordan
Account No for Intermediary bank:	001/095406/02/01
Swift Code:	HBHOJOAX

  
Authorized By:- Eden Engineering  
Muhialdeen Qasim Kawther



Manager Name :- Muhialdeen Qasim  
Manager Title :- Kawther

# Final Report



**Contractor:** Eden Engineering Company.

**Project Name:** Rehabilitation of Al-Hadbaa Association for the Disabled in Mosul

**Location Coordinates:** Latitude: N36°20'33.37"- Longitude: E43°07'02.05"

**Project Period:** 60 days (8 Weeks)

**Start Date:** 17 / 08 / 2010

**Reporting Date:** 20 / 10 / 2010

**Security Situation:** Clear.

**Supplied Materials:** 1- Ordinary cement (3 tons), white cement (0.5 ton).

2- Electrical fixtures (flourcent, 6 No. exhaust fan, cables, 6 No. split type air-conditions, water coolers, 6 No. water boilers.

3- Paints (several colors both emulsion and oil paints).

4- Wooden doors (4 No. teak woods).

5- Glasses 4 mm thickness (100 m<sup>2</sup>).

6- Curtains (300 m<sup>2</sup>).

**Equipments:** Electrical hummers, Grinding machine, Welding machine, Small dumpers and trolleys.

**Achieved Works Percentage:** 100 % according to the last weekly report at 14/10.

**Work Obstruction:** Nil



**Site Engineer**

Yaseen Taha Yaseen

# Daily Report



**Contractor:** Eden Engineering Company.

**Project Name:** Rehabilitation of Al-Hadbaa Association for the Disabled in Mosul

**Location Coordinates:** Latitude: N36°20'33.37"- Longitude: E43°07'02.05"

**Project Period:** 60 days (8 Weeks)      **Elapsed Day:** 32

**Day:** Saturday      **Date:** 18 / 9 / 2010

**Weather & Temp.:** 38° Sunny Day.

**Security Situation:** Clear.

**Supplied Materials:** Nil.

**Manpower:**

**Engineers:** 1      **Technicians:** 1

**Skilled labors:** 15      **Non Skilled labors:** 15

**Equipments:** Electrical hummers (2 No), Grinding machine, Welding machine.

**Achieved Works:** 1- Plastering works on progress.

2- Wiring works on progress(fixing ceiling fans).

3- Painting works on progress.

**Work Obstruction:** Nil.

**Visits:** Nil

**Notes:** Nil



**Site Engineer**

Yaseen Taha Yaseen

# Daily Report



**Contractor:** Eden Engineering Company.

**Project Name:** Rehabilitation of Al-Hadbaa Association for the Disabled in Mosul

**Location Coordinates:** Latitude: N36°20'33.37"- Longitude: E43°07'02.05"

**Project Period:** 60 days (8 Weeks)      **Elapsed Day:** 33

**Day:** Sunday      **Date:** 19 / 9 / 2010

**Weather & Temp.:** 39° Sunny Day.

**Security Situation:** Clear.

**Supplied Materials:** Nil.

**Manpower:**

**Engineers:** 1      **Technicians:** 1

**Skilled labors:** 15      **Non Skilled labors:** 15

**Equipments:** Electrical hummers (2 No), Grinding machine, Welding machine.

**Achieved Works:** 1- Plastering works on progress.


2- Wiring works on progress(fixing ceiling fans).

3- Painting works on progress.

**Work Obstruction:** Nil.

**Visits:** Nil

**Notes:** Nil



**Site Engineer**  
Yaseen Taha Yaseen

# Daily Report



**Contractor:** Eden Engineering Company.

**Project Name:** Rehabilitation of Al-Hadbaa Association for the Disabled in Mosul

**Location Coordinates:** Latitude: N36°20'33.37"- Longitude: E43°07'02.05"

**Project Period:** 60 days (8 Weeks)      **Elapsed Day:** 34

**Day:** Monday      **Date:** 20 / 9 / 2010

**Weather & Temp.:** 41° Sunny Day.

**Security Situation:** Clear.

**Supplied Materials:** Nil.

**Manpower:**

**Engineers:** 1      **Technicians:** 1

**Skilled labors:** 8      **Non Skilled labors:** 14

**Equipments:** Electrical hummers (2 No), Grinding machine, Welding machine.

**Achieved Works:** 1- Plastering works on progress.

2- Wiring works on progress.

3- Painting works on progress.

**Work Obstruction:** Nil.

**Visits:** Nil

**Notes:** Nil



**Site Engineer**  
Yaseen Taha Yaseen



# Daily Report



**Contractor:** Eden Engineering Company.

**Project Name:** Rehabilitation of Al-Hadbaa Association for the Disabled in Mosul

**Location Coordinates:** Latitude: N36°20'33.37"- Longitude: E43°07'02.05"

**Project Period:** 60 days (8 Weeks)      **Elapsed Day:** 35

**Day:** Tuesday.      **Date:** 21 / 9 / 2010

**Weather & Temp.:** 41° Sunny Day.

**Security Situation:** Clear.

**Supplied Materials:** Nil.

**Manpower:**

**Engineers:** 1

**Technicians:** 1

**Skilled labors:** 8

**Non Skilled labors:** 14

**Equipments:** Electrical hummers (2 No), Grinding machine, Welding machine.

**Achieved Works:** 1- Plastering works on progress.


2- Wiring works on progress.

3- Painting works on progress.

**Work Obstruction:** Nil.

**Visits:** Nil

**Notes:** Nil



**Site Engineer**  
Yaseen Taha Yaseen

# Daily Report



**Contractor:** Eden Engineering Company.

**Project Name:** Rehabilitation of Al-Hadbaa Association for the Disabled in Mosul

**Location Coordinates:** Latitude: N36°20'33.37" - Longitude: E43°07'02.05"

**Project Period:** 60 days (8 Weeks)      **Elapsed Day:** 36

**Day:** Wednesday.      **Date:** 22 / 9 / 2010

**Weather & Temp.:** 42° Sunny Day.

**Security Situation:** Clear.

**Supplied Materials:** Nil.

**Manpower:**

**Engineers:** 1      **Technicians:** 1

**Skilled labors:** 5      **Non Skilled labors:** 8

**Equipments:** Electrical hummers (2 No), Grinding machine, Welding machine.

**Achieved Works:** 1- Wiring works on progress.

2- Painting works on progress.

**Work Obstruction:** Nil.

**Visits:** Nil

**Notes:** Nil



**Site Engineer**  
Yaseen Taha Yaseen

# Daily Report



**Contractor:** Eden Engineering Company.

**Project Name:** Rehabilitation of Al-Hadbaa Association for the Disabled in Mosul

**Location Coordinates:** Latitude: N36°20'33.37"- Longitude: E43°07'02.05"

**Project Period:** 60 days (8 Weeks)      **Elapsed Day:** 37

**Day:** Thursday.      **Date:** 23 / 9 / 2010

**Weather & Temp.:** 40° Cloudy Day.

**Security Situation:** Clear.

**Supplied Materials:** Nil.

**Manpower:**

**Engineers:** 1

**Technicians:** 1

**Skilled labors:** 5

**Non Skilled labors:** 8

**Equipments:** Electrical hummers (2 No), Grinding machine, Welding machine.


**Achieved Works:** 1- Wiring works on progress.

2- Painting works on progress.

**Work Obstruction:** Nil.

**Visits:** Nil

**Notes:** Nil



**Site Engineer**

Yaseen Taha Yaseen

# Daily Report



**Contractor:** Eden Engineering Company.

**Project Name:** Rehabilitation of Al-Hadbaa Association for the Disabled in Mosul

**Location Coordinates:** Latitude: N36°20'33.37"- Longitude: E43°07'02.05"

**Project Period:** 60 days (8 Weeks)      **Elapsed Day:** 39

**Day:** Saturday.      **Date:** 25 / 9 / 2010

**Weather & Temp.:** 41° Sunny Day.

**Security Situation:** Clear.

**Supplied Materials:** 1- Ordinary cement (2 tons).  
2- Fluorescent bases ( 27 N0 ).  
3-Exhaust fans (6 No).  
4- Electrical cables for air conditions (50 m.l).

**Manpower:**

**Engineers:** 1      **Technicians:** 1  
**Skilled labors:** 9      **Non Skilled labors:** 15


**Equipments:** Electrical hummers (2 No), Grinding machine, Welding machine.

**Achieved Works:** 1- Plastering works on progress.  
2- Painting works on progress.  
3- Fixing electrical fixtures.  
4- Tilling with porcelain.

**Work Obstruction:** Nil.

**Visits:** Nil

**Notes:** Nil



**Site Engineer**  
Yaseen Taha Yaseen

# Daily Report



**Contractor:** Eden Engineering Company.

**Project Name:** Rehabilitation of Al-Hadbaa Association for the Disabled in Mosul

**Location Coordinates:** Latitude: N36°20'33.37"- Longitude: E43°07'02.05"

**Project Period:** 60 days (8 Weeks)      **Elapsed Day:** 40

**Day:** Sunday.      **Date:** 26 / 9 / 2010

**Weather & Temp.:** 39° Sunny Day.

**Security Situation:** Clear.

**Supplied Materials:** 1- Ordinary cement (1 tons).  
2- Air conditions split type (6 No).

**Manpower:**

**Engineers:** 1      **Technicians:** 1

**Skilled labors:** 8      **Non Skilled labors:** 14

**Equipments:** Electrical hummers (2 No), Grinding machine, Welding machine.

**Achieved Works:** 1- Plastering works on progress.

2- Painting works on progress.

3- Fixing electrical fixtures.


4- Tilling with porcelain.

5- Fixing air conditions.

**Work Obstruction:** Nil.


**Visits:** Nil

**Notes:** Nil



**Site Engineer**  
Yaseen Taha Yaseen

## Daily Report



**Contractor:** Eden Engineering Company.

**Project Name:** Rehabilitation of Al-Hadbaa Association for the Disabled in Mosul

**Location Coordinates:** Latitude: N36°20'33.37"- Longitude: E43°07'02.05"

**Project Period:** 60 days (8 Weeks)      **Elapsed Day:** 41

**Day:** Monday.      **Date:** 27 / 9 / 2010

**Weather & Temp.:** 37° Sunny Day.

**Security Situation:** Clear.

**Supplied Materials:** Nil.

**Manpower:**

**Engineers:** 1      **Technicians:** 1

**Skilled labors:** 7      **Non Skilled labors:** 15

**Equipments:** Electrical hummers (2 No), Grinding machine, Welding machine.  
Small dumper for transporting debris.

**Achieved Works:** 1- Plastering works on progress.

2- Painting works on progress.

3- Fixing electrical fixtures.


4- Tilling with porcelain.

5- Cleaning the site.

**Work Obstruction:** Nil.

**Visits:** Nil


**Notes:** Nil



**Site Engineer**

Yaseen Taha Yaseen

# Daily Report



**Contractor:** Eden Engineering Company.

**Project Name:** Rehabilitation of Al-Hadbaa Association for the Disabled in Mosul

**Location Coordinates:** Latitude: N36°20'33.37"- Longitude: E43°07'02.05"

**Project Period:** 60 days (8 Weeks)      **Elapsed Day:** 42

**Day:** Tuesday.      **Date:** 28 / 9 / 2010

**Weather & Temp.:** 37° Sunny Day.

**Security Situation:** Clear.

**Supplied Materials:** Nil.

**Manpower:**

**Engineers:** 1

**Technicians:** 1

**Skilled labors:** 7

**Non Skilled labors:** 12

**Equipments:** Electrical hummers (2 No), Grinding machine, Welding machine.  
Small dumper for transporting debris.

**Achieved Works:** 1- Painting works on progress.

2- Fixing electrical fixtures.


3- Tilling with porcelain.

4- Cleaning the site.

**Work Obstruction:** Nil.

**Visits:** Nil

**Notes:** Nil



**Site Engineer**  
Yaseen Taha Yaseen

# Daily Report



**Contractor:** Eden Engineering Company.

**Project Name:** Rehabilitation of Al-Hadbaa Association for the Disabled in Mosul

**Location Coordinates:** Latitude: N36°20'33.37"- Longitude: E43°07'02.05"

**Project Period:** 60 days (8 Weeks)      **Elapsed Day:** 43

**Day:** Wednesday.      **Date:** 29 / 9 / 2010

**Weather & Temp.:** 37° Sunny Day.

**Security Situation:** Clear.

**Supplied Materials:** Nil.

**Manpower:**

**Engineers:** 1      **Technicians:** 1

**Skilled labors:** 7      **Non Skilled labors:** 9

**Equipments:** Electrical hummers (2 No), Grinding machine, Welding machine.  
Small dumper for transporting debris.

**Achieved Works:** 1- Painting works on progress.

2- Fixing electrical fixtures.


3- Tilling with porcelain.

4- Cleaning the site.

**Work Obstruction:** Nil.

**Visits:** Nil

**Notes:** Nil



**Site Engineer**

Yaseen Taha Yaseen



# Daily Report



**Contractor:** Eden Engineering Company.

**Project Name:** Rehabilitation of Al-Hadbaa Association for the Disabled in Mosul

**Location Coordinates:** Latitude: N36°20'33.37"- Longitude: E43°07'02.05"

**Project Period:** 60 days (8 Weeks)      **Elapsed Day:** 44

**Day:** Thursday.      **Date:** 30 / 9 / 2010

**Weather & Temp.:** 36° Sunny Day.

**Security Situation:** Clear.

**Supplied Materials:** 1- Water cooler Turkish made.

2- Paints (20 barrel).

3- Wash basin (4 No).

4- White cement ( 500 Kg).

**Manpower:**

**Engineers:** 1

**Technicians:** 1

**Skilled labors:** 7

**Non Skilled labors:** 12

**Equipments:** Electrical hummers (2 No), Grinding machine, Welding machine.

Small dumper for transporting debris.

**Achieved Works:** 1- Painting works on progress.

2- Fixing electrical fixtures.


3- Tilling with porcelain.


4- Cleaning the site.

**Work Obstruction:** Nil.

**Visits:** Nil

**Notes:** Nil



  
**Site Engineer**  
Yaseen Taha Yaseen

# Daily Report



**Contractor:** Eden Engineering Company.

**Project Name:** Rehabilitation of Al-Hadbaa Association for the Disabled in Mosul

**Location Coordinates:** Latitude: N36°20'33.37"- Longitude: E43°07'02.05"

**Project Period:** 60 days (8 Weeks)      **Elapsed Day:** 46

**Day:** Saturday.      **Date:** 2 / 10 / 2010

**Weather & Temp.:** 37° Sunny Day.

**Security Situation:** Clear.

**Supplied Materials:** Nil.

**Manpower:**

**Engineers:** 1      **Technicians:** 1

**Skilled labors:** 7      **Non Skilled labors:** 10

**Equipments:** Electrical hummers (2 No), Grinding machine, Welding machine.  
Small dumper for transporting debris.

**Achieved Works:** 1- Painting works on progress.

2- Fixing electrical fixtures.


3- Fixing wash basin.

4- Cleaning the site.

**Work Obstruction:** Nil.

**Visits:** Nil

**Notes:** Nil

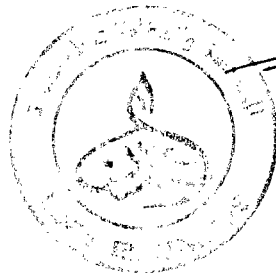

**Site Engineer**  
Yaseen Taha Yaseen

# Daily Report



**Contractor:** Eden Engineering Company.

**Project Name:** Rehabilitation of Al-Hadbaa Association for the Disabled in Mosul

**Location Coordinates:** Latitude: N36°20'33.37"- Longitude: E43°07'02.05"

**Project Period:** 60 days (8 Weeks)      **Elapsed Day:** 47

**Day:** Sunday.      **Date:** 3 / 10 / 2010

**Weather & Temp.:** 37° Sunny Day.

**Security Situation:** Clear.

**Supplied Materials:** 1- Water boiler (6 No).

**Manpower:**

**Engineers:** 1

**Technicians:** 1

**Skilled labors:** 7

**Non Skilled labors:** 10

**Equipments:** Electrical hummers (2 No), Grinding machine, Welding machine.  
Small dumper for transporting debris.

**Achieved Works:** 1- Painting works on progress.

2- Fixing electrical fixtures.


3- Fixing wash basin.

4- Cleaning the site.

**Work Obstruction:** Nil.

**Visits:** Nil

**Notes:** Nil



**Site Engineer**

Yaseen Taha Yaseen

# Daily Report



**Contractor:** Eden Engineering Company.

**Project Name:** Rehabilitation of Al-Hadbaa Association for the Disabled in Mosul

**Location Coordinates:** Latitude: N36°20'33.37"- Longitude: E43°07'02.05"

**Project Period:** 60 days (8 Weeks)      **Elapsed Day:** 48

**Day:** Monday.      **Date:** 4 / 10 / 2010

**Weather & Temp.:** 37° Sunny Day.

**Security Situation:** Clear.

**Supplied Materials:** 1- Water boiler (6 No).

**Manpower:**

**Engineers:** 1      **Technicians:** 1

**Skilled labors:** 6      **Non Skilled labors:** 7


**Equipments:** Electrical hummers (2 No), Grinding machine, Welding machine.  
Small dumper for transporting debris.

**Achieved Works:** 1- Painting works (oil painting for skirting & doors).  
2- Fixing electrical fixtures(boilers,water cooler)&testing.  
4- Cleaning the site.

**Work Obstruction:** Nil.

**Visits:** Nil

**Notes:** Nil



**Site Engineer**  
Yaseen Taha Yaseen

# Daily Report



**Contractor:** Eden Engineering Company.

**Project Name:** Rehabilitation of Al-Hadbaa Association for the Disabled in Mosul

**Location Coordinates:** Latitude: N36°20'33.37"- Longitude: E43°07'02.05"

**Project Period:** 60 days (8 Weeks)      **Elapsed Day:** 49

**Day:** Tuesday.      **Date:** 5 / 10 / 2010

**Weather & Temp.:** 33° Sunny Day.

**Security Situation:** Clear.

**Supplied Materials:** 1- Wooden doors (4No).

**Manpower:**

**Engineers:** 1

**Technicians:** 1

**Skilled labors:** 9

**Non Skilled labors:** 8


**Equipments:** Electrical hummers (2 No), Grinding machine, Welding machine.  
Small dumper for transporting debris.

**Achieved Works:** 1- Painting works (oil painting for skirting ,doors&windows).  
2- Electrical testing.  
3- Fixing wooden doors.  
4- Cleaning the site.

**Work Obstruction:** Nil.

**Visits:** Nil

**Notes:** Nil



**Site Engineer**

Yaseen Taha Yaseen

# Daily Report



**Contractor:** Eden Engineering Company.

**Project Name:** Rehabilitation of Al-Hadbaa Association for the Disabled in Mosul

**Location Coordinates:** Latitude: N36°20'33.37"- Longitude: E43°07'02.05"

**Project Period:** 60 days (8 Weeks)      **Elapsed Day:** 50

**Day:** Wednesday.      **Date:** 6 / 10 / 2010

**Weather & Temp.:** 31° Sunny Day.

**Security Situation:** Clear.

**Supplied Materials:** Nil.

**Manpower:**

**Engineers:** 1

**Technicians:** 1

**Skilled labors:** 9

**Non Skilled labors:** 8


**Equipments:** Electrical hummers (2 No), Grinding machine, Welding machine.  
Small dumper for transporting debris.

**Achieved Works:** 1- Painting works (oil painting for skirting ,doors&windows).  
2- Electrical testing.  
3- Fixing wooden doors.  
4- Cleaning the site.

**Work Obstruction:** Nil.

**Visits:** Nil


**Notes:** Nil



**Site Engineer**

Yaseen Taha Yaseen

# Daily Report



**Contractor:** Eden Engineering Company.

**Project Name:** Rehabilitation of Al-Hadbaa Association for the Disabled in Mosul

**Location Coordinates:** Latitude: N36°20'33.37"- Longitude: E43°07'02.05"

**Project Period:** 60 days (8 Weeks)      **Elapsed Day:** 51

**Day:** Tuesday.      **Date:** 7 / 10 / 2010

**Weather & Temp.:** 32° Sunny Day.

**Security Situation:** Clear.

**Supplied Materials:** Nil.

**Manpower:**

**Engineers:** 1      **Technicians:** 1

**Skilled labors:** 4      **Non Skilled labors:** 10


**Equipments:** Electrical hummers (2 No), Grinding machine, Welding machine.  
Small dumper for transporting debris.

**Achieved Works:** 1- Painting works (oil painting for skirting ,doors&windows).  
2- Cleaning the site.

**Work Obstruction:** Nil.

**Visits:** Nil

**Notes:** Nil



**Site Engineer**  
Yaseen Taha Yaseen

# Daily Report



**Contractor:** Eden Engineering Company.

**Project Name:** Rehabilitation of Al-Hadbaa Association for the Disabled in Mosul

**Location Coordinates:** Latitude: N36°20'33.37"- Longitude: E43°07'02.05"

**Project Period:** 60 days (8 Weeks)      **Elapsed Day:** 53

**Day:** Saturday.      **Date:** 9 / 10 / 2010

**Weather & Temp.:** 32° Sunny Day.

**Security Situation:** Clear.

**Supplied Materials:** 1- Classes (41 M<sup>2</sup>) with paste.

**Manpower:**

**Engineers:** 1

**Technicians:** 1

**Skilled labors:** 6

**Non Skilled labors:** 7

**Equipments:** Electrical hummers (2 No), Grinding machine, Welding machine.  
Small dumper for transporting debris.

**Achieved Works:** 1- Fixing classes.

2- Cleaning the site.

3- Painting.

**Work Obstruction:** Nil.

**Visits:** Nil

**Notes:** Nil



**Site Engineer**

Yaseen Taha Yaseen



# Daily Report



**Contractor:** Eden Engineering Company.

**Project Name:** Rehabilitation of Al-Hadbaa Association for the Disabled in Mosul

**Location Coordinates:** Latitude: N36°20'33.37"- Longitude: E43°07'02.05"

**Project Period:** 60 days (8 Weeks)      **Elapsed Day:** 54

**Day:** Sunday.      **Date:** 10 / 10 / 2010

**Weather & Temp.:** 30° Sunny Day.

**Security Situation:** Clear.

**Supplied Materials:** 1- Curtains.

**Manpower:**

**Engineers:** 1

**Technicians:** 1

**Skilled labors:** 11

**Non Skilled labors:** 12

**Equipments:** Nil.

**Achieved Works:** 1- Fixing classes.

2- Cleaning the site.

3- Painting.


4- Fixing curtains.

5- Grinding façade.

**Work Obstruction:** Nil.

**Visits:** Nil

**Notes:** Nil



**Site Engineer**

Yaseen Taha Yaseen

# Daily Report



**Contractor:** Eden Engineering Company.

**Project Name:** Rehabilitation of Al-Hadbaa Association for the Disabled in Mosul

**Location Coordinates:** Latitude: N36°20'33.37"- Longitude: E43°07'02.05"

**Project Period:** 60 days (8 Weeks)      **Elapsed Day:** 55

**Day:** Monday.      **Date:** 11 / 10 / 2010

**Weather & Temp.:** 22° Cloudy.

**Security Situation:** Clear.

**Supplied Materials:** 1- Curtains.

**Manpower:**

**Engineers:** 1

**Technicians:** 1

**Skilled labors:** 9

**Non Skilled labors:** 13

**Equipments:** Nil.

**Achieved Works:** 1- Fixing classes.

2- Cleaning the site.

3- Painting.

4- Fixing curtains.


5- Grinding façade.

6- Fixing fly mesh.

**Work Obstruction:** Nil.

**Visits:** Nil

**Notes:** Nil



**Site Engineer**

Yaseen Taha Yaseen

# Daily Report



**Contractor:** Eden Engineering Company.

**Project Name:** Rehabilitation of Al-Hadbaa Association for the Disabled in Mosul

**Location Coordinates:** Latitude: N36°20'33.37"- Longitude: E43°07'02.05"

**Project Period:** 60 days (8 Weeks)      **Elapsed Day:** 56

**Day:** Tuesday.      **Date:** 12 / 10 / 2010

**Weather & Temp.:** 22° partly Cloudy.

**Security Situation:** Clear.

**Supplied Materials:** 1- Nil.

**Manpower:**

**Engineers:** 1

**Technicians:** 1

**Skilled labors:** 4

**Non Skilled labors:** 7


**Equipments:** Nil.

**Achieved Works:** 1- Cleaning the site.

**Work Obstruction:** Nil.

**Visits:** Nil

**Notes:** Nil



**Site Engineer**

Yaseen Taha Yaseen

# Daily Report



**Contractor:** Eden Engineering Company.

**Project Name:** Rehabilitation of Al-Hadbaa Association for the Disabled in Mosul

**Location Coordinates:** Latitude: N36°20'33.37"- Longitude: E43°07'02.05"

**Project Period:** 60 days (8 Weeks)      **Elapsed Day:** 57

**Day:** Wednesday.      **Date:** 13 / 10 / 2010

**Weather & Temp.:** 27° Sunny day.

**Security Situation:** Clear.

**Supplied Materials:** 1- Nil.

**Manpower:**

**Engineers:** 1

**Technicians:** 1

**Skilled labors:** 4

**Non Skilled labors:** 7

**Equipments:** Nil.


**Achieved Works:** 1- Cleaning.

2- Checking for all items by UNIDO supervisor engineer.

**Work Obstruction:** Nil.

**Visits:** Nil

**Notes:** Nil



**Site Engineer**

Yaseen Taha Yaseen



## Weekly Report

**Contractor:** Eden Engineering Company.

**Project Name:** Rehabilitation of Al-Hadbaa Association for the Disabled in Mosul.

**Location Coordinates:** Latitude: N36°20'33.37"- Longitude: E43°07'02.05"

**Contract Value:** 73,078.00 USD

**Project Period:** 60 days (8 weeks)

**Start date :** 17/ 8/ 2010


**Week:** Fifth

**Date:** 23/ 9/ 2010

**% of Achieved Works according to the plan:** 70 %

No.	Item Qty. According to BoQ	Achieved Qty.	% of Achieved Item	Remarks
1-1	Removing & replacing new windows .	67 No	7.34 %	
1-2	Building with concrete block for openings.	154 m <sup>2</sup>	7.38 %	
1-3	Plastering.	500 m <sup>2</sup>	8.05 %	
1-4	Painting.	2500 m <sup>2</sup>	7 %	
1-5	Secondary ceiling.	100 m <sup>2</sup>	2.05 %	
1-6	Removal of old tiles.	209m <sup>2</sup>	0.05 %	
1-7	Tilling by porcelain.	65m <sup>2</sup>	2.67 %	
1-9	Garden works.	510 m <sup>2</sup>	1.39 %	
1-11	Stieger tiles for parking area	130 m <sup>2</sup>	2.67 %	
1-12	Installing shade for parking area	L.S	5.48 %	
2-1	Repairing metal doors.	10 No	0.68 %	
2-2	Repairing metal windows.	L.S	4.1 %	

3-1	Repairing plumbing system.	L.S	1.36 %	
3-2	Installing new W.Cs.	11 No	2.26 %	
3-3	Supply & install water tanks.	5 No	1.02 %	
3-4	Tilling.	60 m <sup>2</sup>	2.46 %	
4-1	Wiring and checking.	41 No	3.36 %	
4-2	Wiring and checking and fixing fluorescent fixtures.	130 No	2.67 %	
4-3	Switch –plug (15 Amp).	15 No	0.20 %	
4-11	Supplying material and maintaining distribution bords.	11 No	4.5 %	
<b>TOTAL</b>			<b>66.69 %</b>	



*[Handwritten signature]*

**Site Engineer**  
**Yaseen taha yaseen**



## Weekly Report

**Contractor:** Eden Engineering Company.

**Project Name:** Rehabilitation of Al-Hadbaa Association for the Disabled in Mosul.

**Location Coordinates:** Latitude: N36°20'33.37" - Longitude: E43°07'02.05"

**Contract Value:** 73,078.00 USD

**Project Period:** 60 days (8 weeks)

**Start date :** 17/ 8/ 2010


**Week:** Sixth

**Date:** 30/ 9/ 2010

**% of Achieved Works according to the plan:** 80 %

No.	Item Qty. According to BoQ	Achieved Qty.	% of Achieved Item	Remarks
1-1	Removing & replacing new windows .	67 No	7.34 %	
1-2	Building with concrete block for openings.	154 m <sup>2</sup>	7.38 %	
1-3	Plastering.	700 m <sup>2</sup>	11.5 %	
1-4	Painting.	4000 m <sup>2</sup>	10.95 %	
1-5	Secondary ceiling.	100 m <sup>2</sup>	2.05 %	
1-6	Removal of old tiles.	209m <sup>2</sup>	0.05 %	
1-7	Tilling by porcelain.	165m <sup>2</sup>	6.78 %	
1-9	Garden works.	510 m <sup>2</sup>	1.39 %	
1-11	Stieger tiles for parking area	130 m <sup>2</sup>	2.67 %	
1-12	Installing shade for parking area	L.S	5.48 %	
2-1	Repairing metal doors.	10 No	0.68 %	
2-2	Repairing metal windows.	L.S	4.1 %	

3-1	Repairing plumbing system.	L.S	1.36 %	
3-2	Installing new W.Cs.	11 No	2.26 %	
3-3	Supply& install water tanks.	5 No	1.02 %	
3-4	Tilling.	60 m <sup>2</sup>	2.46 %	
4-1	Wiring and checking.	41 No	3.36 %	
4-2	Wiring and checking and fixing fluorescent fixtures.	170 No	3.49 %	
4-3	Switch –plug (15 Amp).	15 No	0.20 %	
4-4	Exhaust fan.	6 No	0.06 %	
4-5	Switch –plug (32 Amp).	20 No	2.73 %	
4-7	Air condition 2ton capacity.	2 No	1.9 %	
4-11	Supplying material and maintaining distribution bords.	11 No	4.5 %	
<b>TOTAL</b>			<b>83.71 %</b>	



**Site Engineer**  
**Yaseen taha yaseen**





## Weekly Report

**Contractor:** Eden Engineering Company.

**Project Name:** Rehabilitation of Al-Hadbaa Association for the Disabled in Mosul.

**Location Coordinates:** Latitude: N36°20'33.37" - Longitude: E43°07'02.05"

**Contract Value:** 73,078.00 USD

**Project Period:** 60 days (8 weeks)

**Start date :** 17/ 8/ 2010


**Week:** Seventh

**Date:** 7/ 10/ 2010

**% of Achieved Works according to the plan:** 93%


No.	Item Qty. According to BoQ	Achieved Qty.	% of Achieved Item	Remarks
1-1	Removing & replacing new windows .	67 No	7.34 %	
1-2	Building with concrete block for openings.	154 m <sup>2</sup>	7.38 %	
1-3	Plastering.	700 m <sup>2</sup>	11.5 %	
1-4	Painting.	5110 m <sup>2</sup>	14 %	
1-5	Secondary ceiling.	100 m <sup>2</sup>	2.05 %	
1-6	Removal of old tiles.	209m <sup>2</sup>	0.05 %	
1-7	Tilling by porcelain.	165m <sup>2</sup>	6.78 %	
1-8	Oil painting.	300m <sup>2</sup>	0.82 %	
1-9	Garden works.	510 m <sup>2</sup>	1.39 %	
1-10	Grinding facades.	80 m <sup>2</sup>	0.54 %	
1-11	Stieger tiles for parking area	130 m <sup>2</sup>	2.67 %	
1-12	Installing shade for parking area	L.S	5.48 %	

2-1	Repairing metal doors.	10 No	0.68 %	
2-2	Repairing metal windows.	L.S	4.1 %	
2-3	Repairing wooden doors.	10 No	0.68 %	
3-1	Repairing plumbing system.	L.S	1.36 %	
3-2	Installing new W.Cs.	11 No	2.26 %	
3-3	Supply& install water tanks.	5 No	1.02 %	
3-4	Tilling.	60 m <sup>2</sup>	2.46 %	
4-1	Wiring and checking.	41 No	3.36 %	
4-2	Wiring and checking and fixing fluorescent fixtures.	170 No	3.49 %	
4-3	Switch –plug (15 Amp).	15 No	0.20 %	
4-4	Exhaust fan.	6 No	0.61 %	
4-5	Switch –plug (32 Amp).	20 No	2.73 %	
4-6	Supplying water cooler.	1 No	0.54 %	
4-7	Air condition 2ton capacity.	2 No	1.9 %	
4-8	Air condition 1.5ton capacity.	2 No	1.64 %	
4-9	Air condition 1ton capacity.	2 No	1.09 %	
4-10	Water boiler.	6 No	1.23 %	
4-11	Supplying material and maintaining distribution boards.	11 No	4.5 %	
<b>TOTAL</b>			<b>93.85 %</b>	



**Site Engineer**

**Yaseen taha yaseen**



## Weekly Report

**Contractor:** Eden Engineering Company.

**Project Name:** Rehabilitation of Al-Hadbaa Association for the Disabled in Mosul.

**Location Coordinates:** Latitude: N36°20'33.37" - Longitude: E43°07'02.05"

**Contract Value:** 73,078.00 USD

**Project Period:** 60 days (8 weeks)

**Start date :** 17/ 8/ 2010


**Week:** Eighth.

**Date:** 14/ 10/ 2010

**% of Achieved Works according to the plan:** 100%

No.	Item Qty. According to BoQ	Achieved Qty.	% of Achieved Item	Remarks
1-1	Removing & replacing new windows .	67 No	7.33 %	100 %
1-2	Building with concrete block for openings.	154 m2	7.38 %	100 %
1-3	Plastering.	700 m2	11.5 %	100 %
1-4	Painting.	5110 m2	13.98 %	100 %
1-5	Secondary ceiling.	100 m2	2.05 %	100 %
1-6	Removal of old tiles.	209m2	0.57 %	100 %
1-7	Tilling by porcelain.	165m2	6.77 %	100 %
1-8	Oil painting.	630m2	1.72 %	100 %
1-9	Garden works.	510 m2	1.39 %	100 %
1-10	Grinding facades.	160 m2	1.09 %	100 %
1-11	Stieger tiles for parking area	130 m2	2.67 %	100 %
1-12	Installing shade for parking area	L.S	5.47 %	100 %

2-1	Repairing metal doors.	10 No	0.68 %	100 %
2-2	Repairing metal windows.	L.S	4.1 %	100 %
2-3	Repairing wooden doors.	10 No	0.68 %	100 %
2-4	Supplying curtains.	300 m <sup>2</sup>	4.1 %	100 %
3-1	Repairing plumbing system.	L.S	1.37 %	100 %
3-2	Installing new W.Cs.	11 No	2.26 %	100 %
3-3	Supply& install water tanks.	5 No	1.03 %	100 %
3-4	Tilling.	60 m2	2.46 %	100 %
4-1	Wiring and checking.	41 No	3.36 %	100 %
4-2	Wiring and checking and fixing fluorescent fixtures.	170 No	3.49 %	100 %
4-3	Switch –plug (15 Amp).	15 No	0.20 %	100 %
4-4	Exhaust fan.	6 No	0.61 %	100 %
4-5	Switch –plug (32 Amp).	20 No	2.73 %	100 %
4-6	Supplying water cooler.	1 No	0.55 %	100 %
4-7	Air condition 2ton capacity.	2 No	1.91 %	100 %
4-8	Air condition 1.5ton capacity.	2 No	1.64 %	100 %
4-9	Air condition 1ton capacity.	2 No	1.09 %	100 %
4-10	Water boiler.	6 No	1.23 %	100 %
4-11	Supplying material and maintaining distribution boards.	11 No	4.51 %	100 %
<b>TOTAL %</b>			<b>100 %</b>	



*(Handwritten signature)*

**Site Engineer**

**Yaseen taha yaseen**



בתיאטרון חיפה







معهد الدراسات والبحوث

































































































































## **Photos before the rehabilitation**



















































## **Photos after the rehabilitation**





































